

TOWN OF WHITBY

# Whitby Sports Complex Project

Status Update #1 | February 1, 2024



[connectwhitby.ca/SportsComplex](https://connectwhitby.ca/SportsComplex)

Whitby 


# PROJECT OVERVIEW

The Whitby Sports Complex (WSC) is located on 26 acres of land on the west side of Baldwin Street South, south of the intersection of Highway 407. The WSC is comprised of a new 160,000 square feet two-story recreation facility and new park space. The total approved budget for the project is \$154,853,886.

Ledcor Construction Ltd (LCL) was awarded the construction contract of \$125,655,001 in August 2023. LCL began construction on August 28, 2023. The anticipated occupancy date is December 2025.

## Construction Statistics

- \$9,359,000 of \$125,655,001 billed to date
- 7.5% complete construction
- 23 months of construction remaining (4% per month)

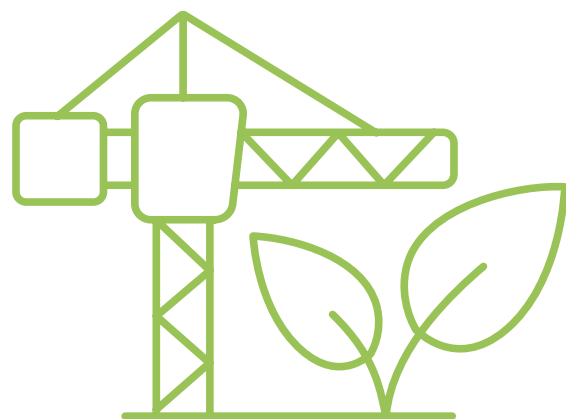

The WSC is a  
key action item  
of Whitby's  
Community  
Strategic Plan

## Construction Progress to Date

### Excavation and Site Services

- Approximately 70% of the site grading and excavation is complete
- Underground stormwater piping is underway and is approximately 25% complete

### Arena B (East Pad)

- Structural below grade footings are approximately 95% complete
- The east wall is currently being formed and is anticipated to be completed in February

### Arena A (West Pad)

- Structural below-grade footings are approximately 30% complete

### Arena Dressing Rooms

- Structural below grade footings are 100% complete
- The walls are approximately 50% complete

### Gymnasium

- Structural below grade footings are 90% complete

### Pool


- Structural soil work (shoring) is underway, and LCL is anticipated to be excavated to the bottom of the pool footprint in March 2024

# UPCOMING CONSTRUCTION MILESTONES



## Winter 2024

- ▶ Geothermal borehole drilling is scheduled to start in early February.



## Spring/Summer 2024

- ▶ Structural steel installation for the walls and roof at the gymnasium and arenas are targeted to begin in early April 2024.
- ▶ Park construction for the program spaces is anticipated to begin in summer 2024.



## Fall 2024

- ▶ Pool structural floors and walls are anticipated to be installed from the basement to the 2nd floor in September 2024

# CONSTRUCTION SITE PROGRESS



Arena B

Dressing  
Rooms

Arena A

Pool

Double Gymnasium

Aerial North View  
(Jan 7, 2024)

# CONSTRUCTION SITE PROGRESS



Gymnasium Footings



Arena Dressing Room Wall



Arena B Footings



Stormwater Servicing



Arena B Wall Reinforcement



Pool Shoring Installation



Gymnasium

Arena A

Pool

Dressing Rooms

Arena B

Aerial East View  
(Jan 7, 2024)

# CONSTRUCTION SITE PROGRESS



Arena B Winter Protection



Arena A North Footings



Dressing Room West Wall



Arena B Wall Formwork



Dressing Room Walls



Arena A Northwest Footings

**Prepared by: Community Services (CMS)**  
**Report Period: September 2023 to January 2024**  
**Next Report: May 2024**



Event Plaza Space
